


3.1 Cronograma de trabajo GANTT



3.2 Cronograma de trabajo **Tareas Nivel 1 – Análisis & Diseño**

	Name	Start	Finish	Late Start	Late Finish
0	▼ JCE	Apr 7, 2022 at...	Aug 22, 2022 at...	Mar 30, 2022 at...	Aug 22, 2022 at...
1	▼ Licitacion JCE	Apr 7, 2022 at...	Aug 5, 2022 at...	Mar 30, 2022 at...	Aug 22, 2022 at...
2	Aprobacion inicio	Apr 7, 2022 at 8...	Apr 7, 2022 at 5...	Apr 7, 2022 at 8...	Apr 7, 2022 at 5...
3	▼ Analisis y diseño	Apr 8, 2022 at...	Apr 14, 2022 at...	Mar 30, 2022 at...	Aug 22, 2022 at...
4	Diseño gráfico	Apr 8, 2022 at 8...	Apr 14, 2022 at...	Aug 15, 2022 at...	Aug 22, 2022 at...
5	Nomenclatura de tickets	Apr 8, 2022 at 8...	Apr 12, 2022 at...	Aug 17, 2022 at...	Aug 22, 2022 at...
6	Definición de arquitectura	Apr 8, 2022 at 8...	Apr 14, 2022 at...	Mar 30, 2022 at...	Apr 6, 2022 at 2...
7	▼ Servicios Core	Apr 15, 2022 at...	May 12, 2022 a...	Jul 25, 2022 at...	Aug 22, 2022 at...
8	Creación de servicio	Apr 15, 2022 at...	May 10, 2022 at...	Jul 25, 2022 at...	Aug 18, 2022 at...
9	Modificar servicio	May 10, 2022 at...	May 12, 2022 at...	Aug 18, 2022 at...	Aug 22, 2022 at...
10	Borrar servicio	May 10, 2022 at...	May 12, 2022 at...	Aug 18, 2022 at...	Aug 22, 2022 at...
11	► Desarrollo UI	Apr 15, 2022 at...	Jul 4, 2022 at 5...	Apr 8, 2022 at...	Aug 22, 2022 at...
38	► Desarrollo CRUD	Apr 15, 2022 at...	Aug 5, 2022 at...	Apr 6, 2022 at...	Aug 22, 2022 at...
62	► Servicios complementarios	Jul 1, 2022 at 8...	Aug 9, 2022 at...	Jul 1, 2022 at 8...	Aug 22, 2022 at...
77	Pruebas unitarias	Aug 9, 2022 at...	Aug 15, 2022 at...	Aug 9, 2022 at...	Aug 15, 2022 at...
78	Entrenamiento	Aug 16, 2022 at...	Aug 17, 2022 at...	Aug 19, 2022 at...	Aug 22, 2022 at...
79	Documentacion	Aug 16, 2022 at...	Aug 22, 2022 at...	Aug 16, 2022 at...	Aug 22, 2022 at...
80	Entrega final	Aug 22, 2022 at...	Aug 22, 2022 at...	Aug 22, 2022 at...	Aug 22, 2022 at...

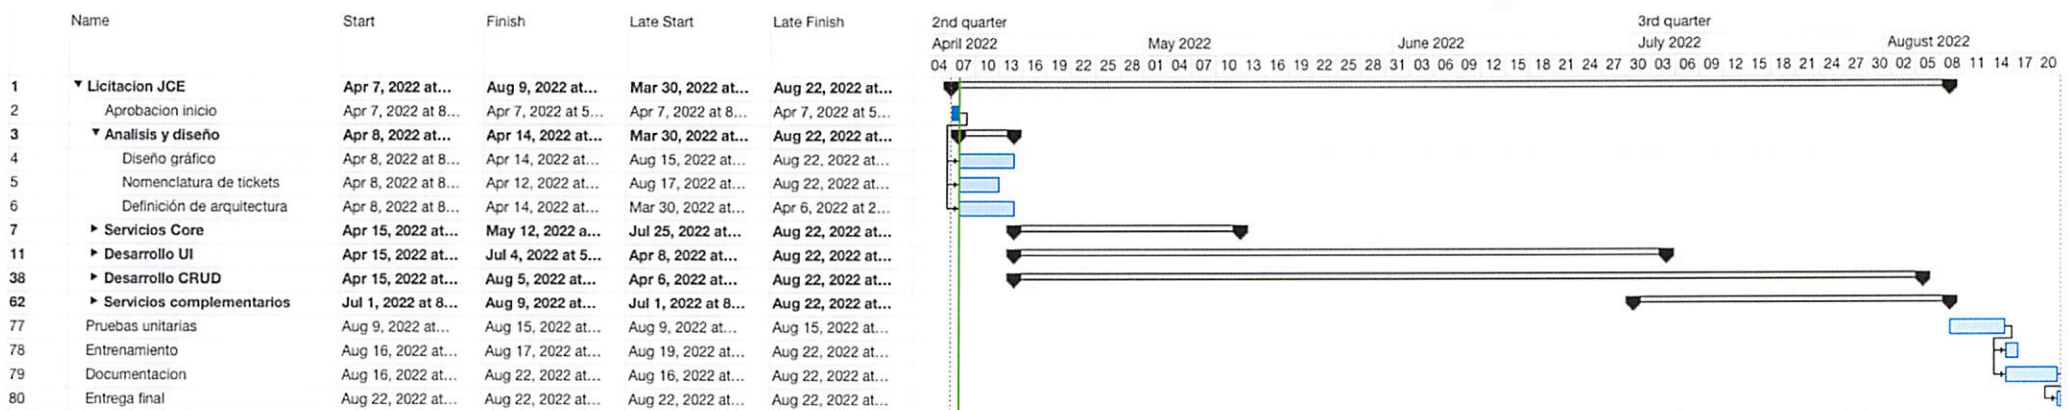

PROPUESTA TECNICA LICITACION

REFERENCIA: JCE-CCC-LPN-2022-0002

